




OLD CUTLER ROADWAY IMPROVEMENTS

phase **4**

- Phase 1** > Marlin Drive to SW 92nd Avenue
- Phase 2** > SW 92nd Avenue to Franjo Road
- Phase 3** > Franjo Road to SW 87th Avenue
- Phase 4** > SW 97th Ave. to Marlin Drive
- Phase 5** > Roundabout SW 97th Ave. Roundabout SW 87th Ave.

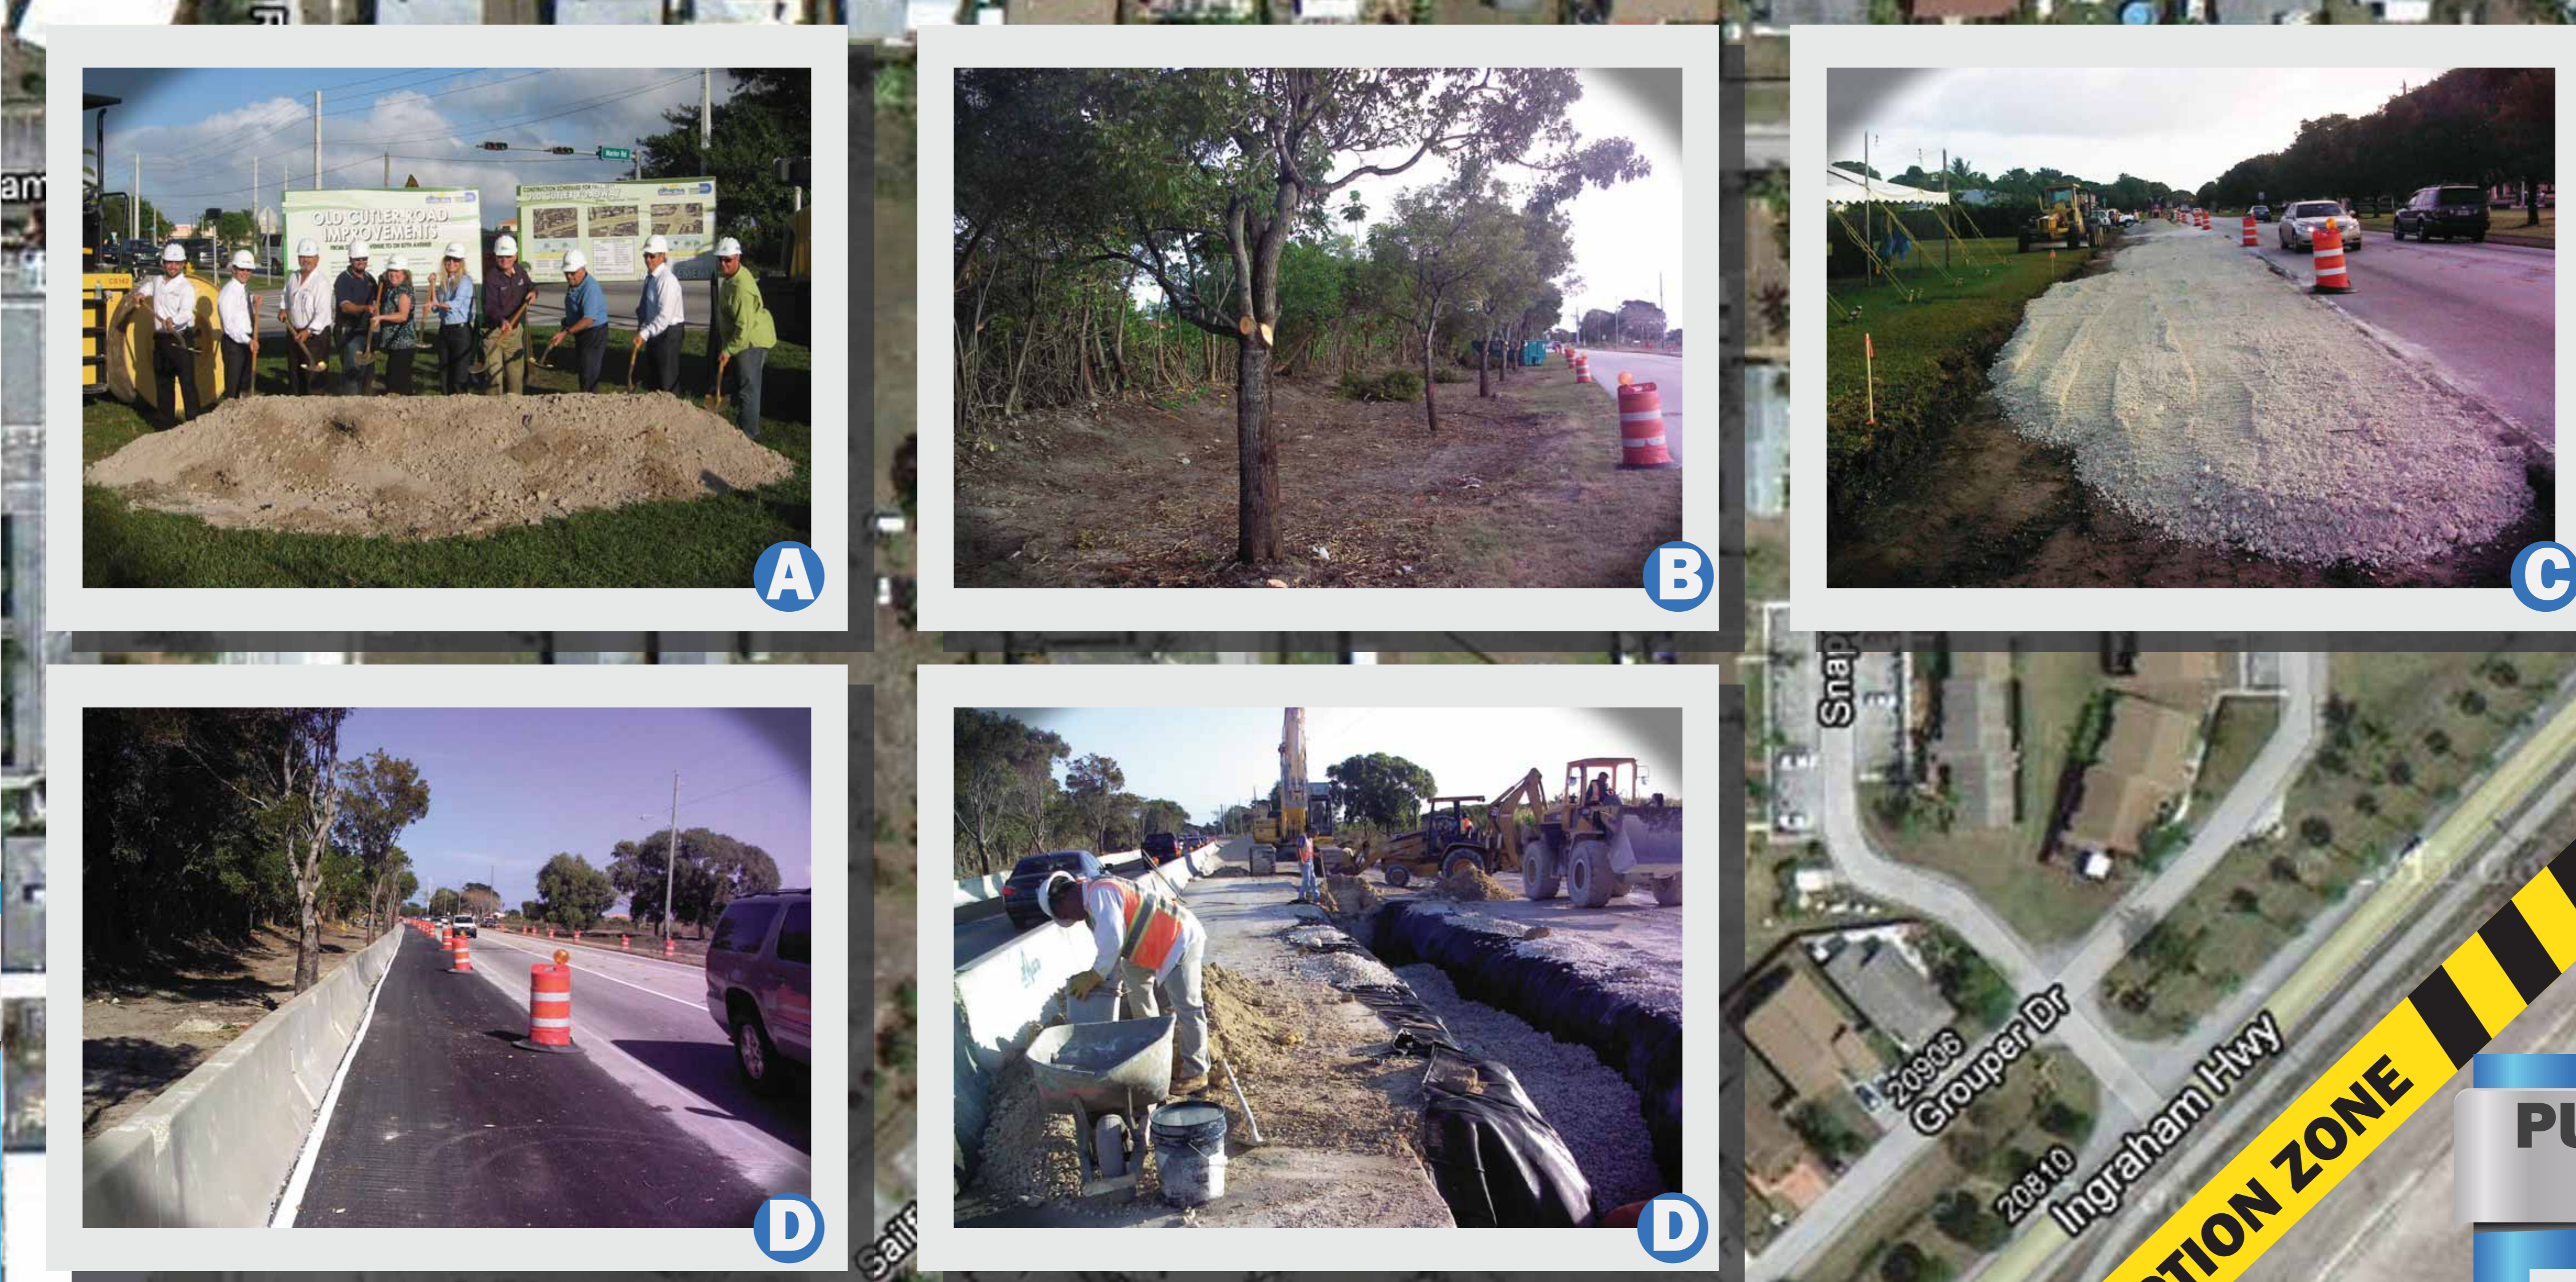

MILESTONES JANUARY 2012

- A** **Ground Breaking**
November 16, 2011
- B** **WEEK ENDING DEC 23, 2011**
 - Contractor mobilized to site
 - Clearing/grubbing vegetation
 - Completed the root pruning of the trees and relocated palm trees
 - Trimmed Trees
- C** **WEEK ENDING JAN 6, 2012**
 - Set up MOT for shoulder work - SB
 - Placed lime rock preparing for widening of MOT - Old Cutler Road (west side)
 - Lay out limits of construction at SW 93rd Ave.
 - Started to tack coat and prime lime rock
- D** **WEEK ENDING JAN 13, 2012**
 - Installed temporary concrete-wall barrier along work zone and shifted traffic lanes
 - Commenced installation of drainage structures

PUBLIC INVOLVEMENT ACTIVITIES

- Ground Breaking**
November 16, 2011
- WEEK ENDING DEC 23, 2011**
 - Town's Public Works Director (PWD) and Marlin's Public Involvement Plan Project Manager (PIPM), met and agreed on public outreach details to be used during construction phase.
- WEEK ENDING JAN 6, 2012**
 - The "Town of Cutler Bay" received a strategic "Public Involvement Plan" (PIP).
 - PWD & PIPM met with the Sansone Group in reference to the Old Cutler Towne Shopping Center's anticipated needs for next phase.
- WEEK ENDING JAN 13, 2012**
 - PIPM replied to concerns from the Cutler Ridge United Methodist Church.



Marlin Engineering, Inc.

E-MAIL YOUR COMMENTS/QUESTIONS:
oldcutlerroadimprovements@cutlerbay-fl.gov



OLD CUTLER ROADWAY IMPROVEMENTS

CONSTRUCTION SCHEDULE

2012

2013

PROJECT DURATION

